



Vendor: CompTIA

Exam Code: PK0-003

Exam Name: CompTIA Project+ Certification Exam

Version: Demo

QUESTION 1

There is a minor conflict between several members on a project team; the issue has no significant impact on the project. Which of the following would be the BEST conflict resolution technique for the project manager to employ?

- A. Avoiding
- B. Forcing
- C. Compromising
- D. Confronting

Correct Answer: A

QUESTION 2

A customer has requested an increase in the scope of a current project, but the project schedule remains the same. Which of the following is MOST likely impacted? (Select TWO).

- A. Project quality
- B. Project cost
- C. Project baseline
- D. Project milestones
- E. Deployment plan

Correct Answer: AB

QUESTION 3

Which of the following would be used to allow a project team to take action to fix problems that are causing the GREATEST number of defects?

- A. Flow charting
- B. Statistical sampling
- C. Scatter diagram
- D. Pareto diagram

Correct Answer: D

QUESTION 4

Which of the following risk response strategies involves the use of insurance, performance bonds, or warranties?

- A. Risk acceptance
- B. Risk mitigation

- C. Risk avoidance
- D. Risk transfer

Correct Answer: D

QUESTION 5

During which of the following process groups is the availability of required resources for the project determined?

- A. Executing
- B. Monitoring/Controlling
- C. Initiating
- D. Planning

Correct Answer: D

QUESTION 6

Given the circumstances below, which of the following would be the BEST action for the project manager to take?

- One of the key stakeholders disagrees with the project.
 - Two of the key staff members refuse to work with each other.
 - The budget for the project has been reduced.
 - The scope of the project has changed.
- A. The staff members who refuse to work together should be terminated so that the project can proceed on schedule.
 - B. The project should be closed because the scope has changed.
 - C. The project manager should work with the stakeholders to resolve the areas of disagreement.
 - D. The project manager should fast track the schedule because the project budget was reduced.

Correct Answer: C

QUESTION 7

A product does not meet the customer's quality specifications. Which of the following can the project manager use to bring the product quality into alignment with the specifications? (Select TWO).

- A. Fast tracking
- B. Trend analysis

- C. Pareto chart
- D. High level cost estimate
- E. Monte Carlo

Correct Answer: BC

QUESTION 8

A key stakeholder has informed the project manager that the project must be completed on time. The project is currently running behind schedule. The budget provided for the project will not allow for additional resources. In order to meet the demands of the key stakeholder, which of the following is the BEST action for the project manager to take?

- A. Crash the schedule.
- B. Fast track the schedule.
- C. Negotiate for more resources.
- D. Negotiate a new schedule.

Correct Answer: B

QUESTION 9

The key stakeholder requires the project manager to advance the completion date before funding runs out. The project manager has had problems with this stakeholder in the past and wants to document this request. Which of the following should the project manager do? (Select TWO).

- A. Complete a project change request form.
- B. Analyze the project impact.
- C. Update the project scope statement.
- D. Revise the scope management plan.
- E. Monitor the work performance.

Correct Answer: AB

QUESTION 10

During a project status meeting a positive project risk is identified and is within the team's control. Which of the following would be the BEST response?

- A. Accept the risk.
- B. Transfer the risk.
- C. Mitigate the risk.
- D. Exploit the risk.

Correct Answer: D

QUESTION 11

The project manager has the MOST authority in which of the following organizational structures?

- A. Balanced Matrix
- B. Functional
- C. Weak Matrix
- D. Strong Matrix

Correct Answer: D

QUESTION 12

A project sponsor has just signed a document that authorizes the project manager for an upcoming project. Which of the following elements would be included in this document?

- A. The purpose of the project.
- B. Quantitative analysis for all major project risks.
- C. Team member responsibilities.
- D. The technical specifications of the final deliverable.

Correct Answer: A

QUESTION 13

A project has just entered the execution phase. The deadline to respond to the RFP has expired. Which of the following activities describes the NEXT action to take?

- A. Develop a contract for each vendor.
- B. Perform a make or buy analysis.
- C. Determine the type of contract for the project.
- D. Evaluate and select a seller response.

Correct Answer: D

QUESTION 14

A project manager has just completed the work breakdown structure (WBS) with the project team. Which of the following would be used during activity sequencing?

- A. Precedence diagramming method
- B. Monte Carlo analysis

- C. Resource availability
- D. Resource leveling technique

Correct Answer: A

QUESTION 15

Fast tracking a schedule involves which of the following?

- A. Adding resources to critical path activities.
- B. Increasing the budget for the project.
- C. Allowing team members to work overtime.
- D. Performing critical path activities simultaneously.

Correct Answer: D

QUESTION 16

Crashing a schedule involves which of the following?

- A. Performing a re-baseline of the project schedule.
- B. Performing critical path activities simultaneously.
- C. Adding resources to critical path activities.
- D. Estimating the earned value of the project activities.

Correct Answer: C

QUESTION 17

A project with a total budget of \$100,000 is in the ninth month and has an earned value of \$80,000 and actual costs of \$90,000. The project's cost variance is:

- A. -\$5,000.
- B. -\$10,000.
- C. +\$10,000.
- D. +\$170,000.

Correct Answer: B

QUESTION 18

During which of the following process groups is the project charter developed?

- A. Pre-project setup

- B. Project execution
- C. Project planning
- D. Project control

Correct Answer: A

QUESTION 19

Which of the following describes a work breakdown structure (WBS)?

- A. Determines the critical path of a project schedule.
- B. Identifies stakeholders and their roles.
- C. Is deliverable-oriented and hierarchical in nature.
- D. Measures the quality of the project objectives.

Correct Answer: C

QUESTION 20

During the execution phase, a customer approaches the project manager demanding a change. Which of the following are the steps the project manager should take? (Select TWO).

- A. Make the change.
- B. Notify the Executive Sponsor.
- C. Fill out a change request form.
- D. Evaluate the impact of the change.
- E. Deny the change.

Correct Answer: CD

QUESTION 21

A project team member has been re-assigned to another project. Which of the following should the project manager do FIRST?

- A. Notify the executive sponsor of the team member's reassignment.
- B. Assess the impact on the project schedule.
- C. Request additional funds to pay overtime to the remaining team members.
- D. Request additional staff to complete the work of the re-assigned team member.

Correct Answer: B

QUESTION 22

During execution of the project, the project sponsor informs the project manager that a requirement needs to be added to the scope statement. Which of the following is the FIRST action that the project manager should take?

- A. Evaluate the impact of the change on the project.
- B. Call the project team members together to determine how to handle the change.
- C. Change the work breakdown structure (WBS) to include all the tasks involved with this change.
- D. Rewrite the statement of work (SOW) to include the proposed change.

Correct Answer: A

QUESTION 23

Which of the following are reasons why formal project closure is important? (Select THREE).

- A. Releases staff from the project.
- B. Reassigns staff to another project.
- C. Releases leftover funding from the project.
- D. Provides historical information.
- E. Allows for final changes to the work breakdown structure (WBS).
- F. Confirms completed/non-completed objectives.

Correct Answer: ADF

QUESTION 24

Which of the following is the correct order of the project life cycle?

- A. Planning, initiating, monitoring / controlling, executing, closing.
- B. Initiating, planning, monitoring / controlling, executing, closing.
- C. Initiating, planning, executing, monitoring / controlling, closing.
- D. Planning, initiating, executing, monitoring / controlling, closing.

Correct Answer: C

QUESTION 25

Various technologies exist to complete a project, but the project manager is not well versed in these technologies. Which of the following can the project manager initiate to assist with the decision?

- A. A Statement of Work (SOW)

- B. A project needs assessment
- C. A vendor contract
- D. A Request for Proposal (RFP)

Correct Answer: D

QUESTION 26

A project manager receives an inquiry from the human resources department about the work ethic of a certain team member. Which of the following should the project manager give to the HR department?

- A. Performance reports
- B. Meeting attendance
- C. Key Performance Indicators (KPIs)
- D. Quality metrics

Correct Answer: A

QUESTION 27

A new technology being implemented will result in project team member layoffs. Which of the following actions can the project manager take to address team member concerns?

- A. Cancel the project.
- B. Host a meeting to provide a status update.
- C. Outsource the project.
- D. Select a different technology that will not result in layoffs.

Correct Answer: B

QUESTION 28

A company is validating a project. The project has a high probability of success. Which of the following is the MOST important consideration before authorizing the project?

- A. The company's strategic goals
- B. Training requirements
- C. The project manager's experience
- D. Resource availability

Correct Answer: A

QUESTION 29

A department has had several absences due to illness; as a result, the project team has not been meeting the set milestones. Which of the following techniques would assist the project manager to determine the affect on the project schedule?

- A. CPI
- B. SV
- C. PV
- D. EV

Correct Answer: B

QUESTION 30

Which of the following is an advantage of a functional organization?

- A. Centralization of resources.
- B. Increase of the project manager's authority.
- C. Functional manager controls resources.
- D. Decrease in overlap of projects.

Correct Answer: A

QUESTION 31

A company has 50 percent of a project complete. The project plan states:

- The project will last 10 months
- The company will create 150 gadgets per month
- The cost to make each gadget will be \$55
- The total budget is \$9,000

Which of the following is the planned value for the project?

- A. \$1,500
- B. \$4,500
- C. \$8,250
- D. \$9,000

Correct Answer: B

QUESTION 32

Which of the following is included in the project charter?

- A. A work performance report
- B. A cost assessment
- C. A high level plan
- D. A risk assessment

Correct Answer: C

QUESTION 33

Which of the following activities occur in the planning phase of a project? (Select TWO).

- A. Obtain product acceptance.
- B. Identify the Executive Sponsor.
- C. Assign and explain tasks.
- D. Perform project kick off.
- E. Prepare a project charter.

Correct Answer: CD

QUESTION 34

Transition plans include which of the following elements?

- A. Work Breakdown Structure (WBS)
- B. Project warranty
- C. Project process reports
- D. Earned value calculations

Correct Answer: B

QUESTION 35


Which of the following tools can be used to determine if a project deliverable is out of specification?

- A. PERT
- B. RACI chart
- C. Gantt chart
- D. Control chart

Correct Answer: D

QUESTION 36

Click on the Exhibit button. Which of the following is the critical path of the network diagram?

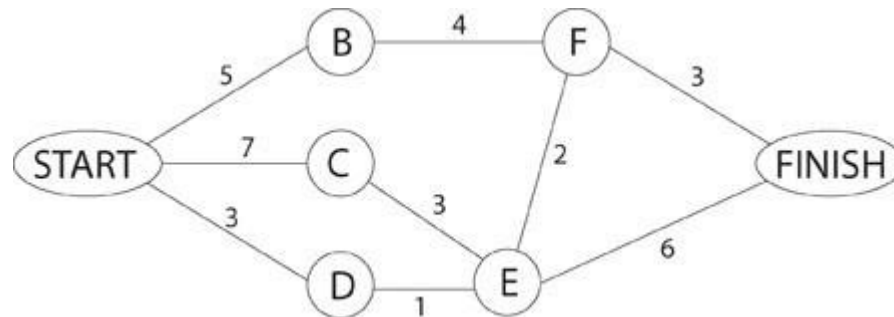

- A. Start-D-E-Finish
- B. Start-C-E-Finish
- C. Start-D-E-F-Finish
- D. Start-B-F-Finish

Correct Answer: B

QUESTION 37

During monitoring/controlling, a defect is found in the project deliverable. In which of the following processes did this occur?

- A. Quality control
- B. Risk assessment
- C. Quality assurance
- D. Stakeholder analysis

Correct Answer: A

QUESTION 38

A project manager needs to determine the trends a process is exhibiting over time. Which of the following tools should the project manager use?

- A. Histogram
- B. Ishikawa diagram
- C. Pareto chart
- D. Run chart

Correct Answer: D

QUESTION 39

A project manager conducted a risk probability and impact assessment with the project team. In which of the following risk management processes did this occur?

- A. Qualitative risk analysis
- B. Quantitative risk analysis
- C. Risk response planning
- D. Risk identification

Correct Answer: A

QUESTION 40

One of the team members assigned to a project is not performing well. The team member is new and is not experienced in the type of work involved with this project. Which of the following is the BEST response to this situation?

- A. Ask other team members to help.
- B. Assign the team member to another project.
- C. Talk to the team member to encourage better performance.
- D. Arrange for training for the team member.

Correct Answer: D

EnsurePass.com Members Features:

1. Verified Answers researched by industry experts.
2. Q&As are downloadable in PDF and VCE format.
3. 98% success Guarantee and **Money Back** Guarantee.
4. Free updates for **180** Days.
5. **Instant Access to download the Items**

View list of All Exam provided:

<http://www.ensurepass.com/certifications?index=A>

To purchase Lifetime Full Access Membership click here:

<http://www.ensurepass.com/user/register>

Valid Discount Code for 2015: JREH-G1A8-XHC6

To purchase the HOT Exams:

<u>Cisco</u>		<u>CompTIA</u>		<u>Oracle</u>	<u>VMWare</u>	<u>IBM</u>
100-101	640-554	220-801	LX0-101	1Z0-051	VCAD510	C2170-011
200-120	200-101	220-802	N10-005	1Z0-052	VCP510	C2180-319
300-206	640-911	BR0-002	SG0-001	1Z0-053	VCP550	C4030-670
300-207	640-916	CAS-001	SG1-001	1Z0-060	VCAC510	C4040-221
300-208	640-864	CLO-001	SK0-003	1Z0-474	VCP5-DCV	RedHat
350-018	642-467	ISS-001	SY0-301	1Z0-482	VCP510PSE	EX200
352-001	642-813	JK0-010	SY0-401	1Z0-485		EX300
400-101	642-832	JK0-801	PK0-003	1Z0-580		
640-461	642-902			1Z0-820		

