

[Download Full Version Prince2-Practitioner Exam Dumps\(Updated in Feb/2023\)](#)

Initial estimates indicated that the project would cost £2.5m and take two years to complete.

MFH senior management agreed that there was a case for outsourcing, and accepted the recommendations as a basis for the project. There is an expected saving of £20m over 10 years.

The Outsourcing project has completed the Starting up a Project process and is now in the initiation stage. Because of the strategic importance of the project, the MFH Chief Executive Officer has taken the role of Executive. A PRINCE2-experienced Project Manager has been appointed from within MFH. Staff within the business functions being outsourced will work with the external consultants who conducted the feasibility study to define the detailed designs.


Which 2 statements should be recorded under the Timescale heading?

- A. The contract with the selected service provider will be agreed during stage 3.
- B. The expected benefits will be calculated over 10 years from completion of the project.
- C. If more MFH divisions are added to the scope of the services to be outsourced, the project timescale will be extended and the realization of benefits will be delayed.
- D. The expected benefits should start to be realized as soon as the outsourced services become operational at the end of stage 4.
- E. The transfer of equipment and staff is estimated to take six weeks.

Correct Answer: AB

QUESTION 28

Additional Information

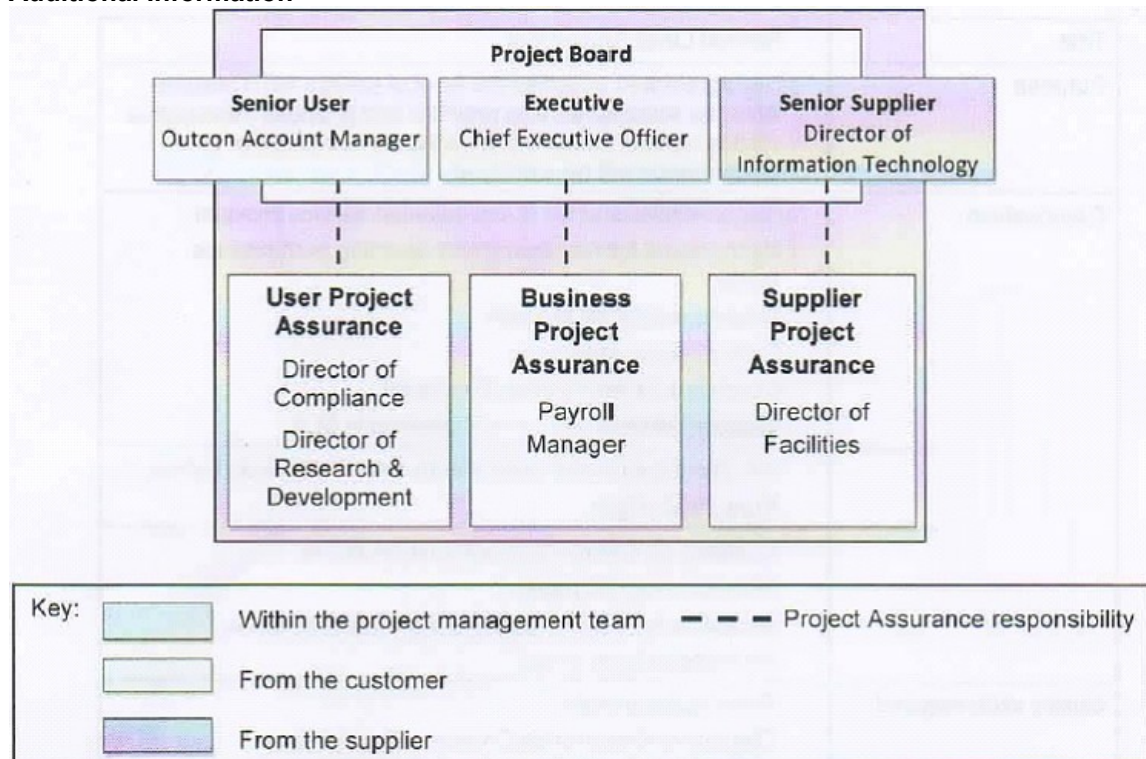

Further information on some resources who could be involved in the project:

Outcome Account Manager: He represents Outcome which is a recruitment agency that provides specialist outsourcing resources. Outcome provided the consultants who carried out the feasibility

[Download Full Version Prince2-Practitioner Exam Dumps\(Updated in Feb/2023\)](#)

study and the same consultants will be providing support and guidance to the Information Technology and Facilities teams during the project.

Director of Finance Division: She was transferred from the Information Technology Division 12 months ago. She is responsible for ensuring a cost-conscious approach is adopted in all operational and project activities across the Ministry of Food Hygiene.

Hardware Manager: Reports to the Director of Information Technology. He provides computer hardware to all business functions but has little awareness of the needs of his colleagues working in software.

Payroll Manager: Reports to the Director of Finance. He is a very experienced and efficient qualified accountant who has much of the responsibility of running the Finance Division on behalf of the Director of Finance. He has been involved in drafting the Ministry's business strategy and assisting in a full business risk assessment. He also drafted the corporate Business Case standards.

Which 2 alternative actions apply to the proposed Senior Supplier for this project?

- A. Retain because she is responsible for the design of the future Information Technology organization and working practices.
- B. Add 'Director of Facilities' because he is responsible for the design of the future organization, processes, systems and operation models for Facilities.
- C. Add 'Hardware Manager' because he provides computer hardware to all business functions and will be impacted by the outcome.
- D. Remove because she only represents the Information Technology Division.
- E. Replace with 'Director of Facilities' because he supports the initiative and has many ideas about how to improve the service.

Correct Answer: AB

QUESTION 29

Which of the following is False?


A Successful project management team should.

- A. Have business, user and supplier stakeholder representation
- B. Never be reviewed as members should stay with the team for the duration
- C. Ensure appropriate governance by defining responsibilities for directing, managing and delivering the project and clearly defining accountability at all levels
- D. Have an effective strategy to manage communication flows to and from stakeholders

Correct Answer: B

QUESTION 30

Additional Information

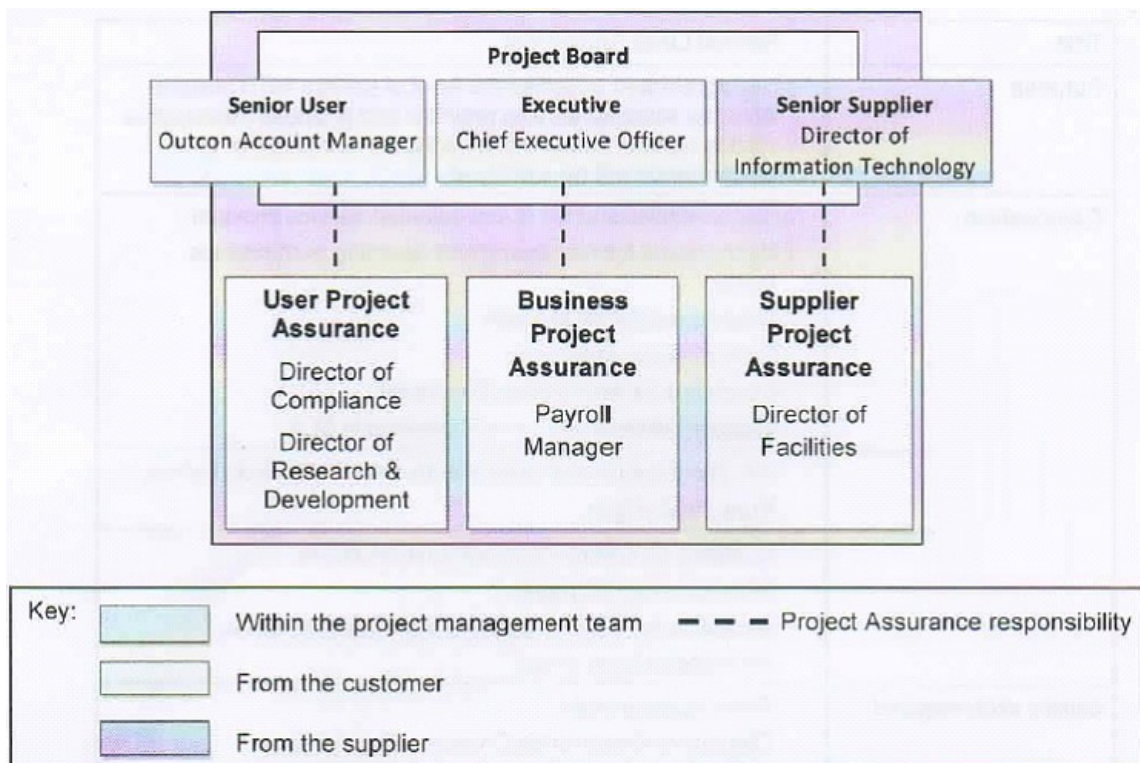

Further information on some resources who could be involved in the project:

Outcome Account Manager: He represents Outcome which is a recruitment agency that provides specialist outsourcing resources. Outcome provided the consultants who carried out the feasibility study and the same consultants will be providing support and guidance to the Information Technology and Facilities teams during the project.

Director of Finance Division: She was transferred from the Information Technology Division 12 months ago. She is responsible for ensuring a cost-conscious approach is adopted in all operational and project activities across the Ministry of Food Hygiene.

Hardware Manager: Reports to the Director of Information Technology. He provides computer hardware to all business functions but has little awareness of the needs of his colleagues working in software.

Payroll Manager: Reports to the Director of Finance. He is a very experienced and efficient qualified accountant who has much of the responsibility of running the Finance Division on behalf of the Director of Finance. He has been involved in drafting the Ministry's business strategy and assisting in a full business risk assessment. He also drafted the corporate Business Case standards.

Which 2 alternative actions apply to the proposed Senior User for this project?

- A. Retain because he provides the outsourcing resources required to support the project.
- B. Replace with 'Director of Research and Development' because she deals with both the Information Technology and the Facilities Divisions and can make sure her division's needs are specified.
- C. Remove because he has no authority to commit user resources.
- D. Add 'Hardware Manager' because he provides computer hardware to all business functions and will be impacted by the outcome.

[Download Full Version Prince2-Practitioner Exam Dumps\(Updated in Feb/2023\)](#)

- E. Retain because he will be providing support to the Information Technology and Facilities teams during the project.

Correct Answer: BC

QUESTION 31


Which of the following represents the four key characteristics a good Project board should display?

- A. Authority, Credibility, Commitment, Availability
- B. Authority, Credibility, Delegation, Availability
- C. Authority, Availability, Connections, Delegation
- D. Authority, Credibility, Connections, Delegation

Correct Answer: B

QUESTION 32

Additional Information

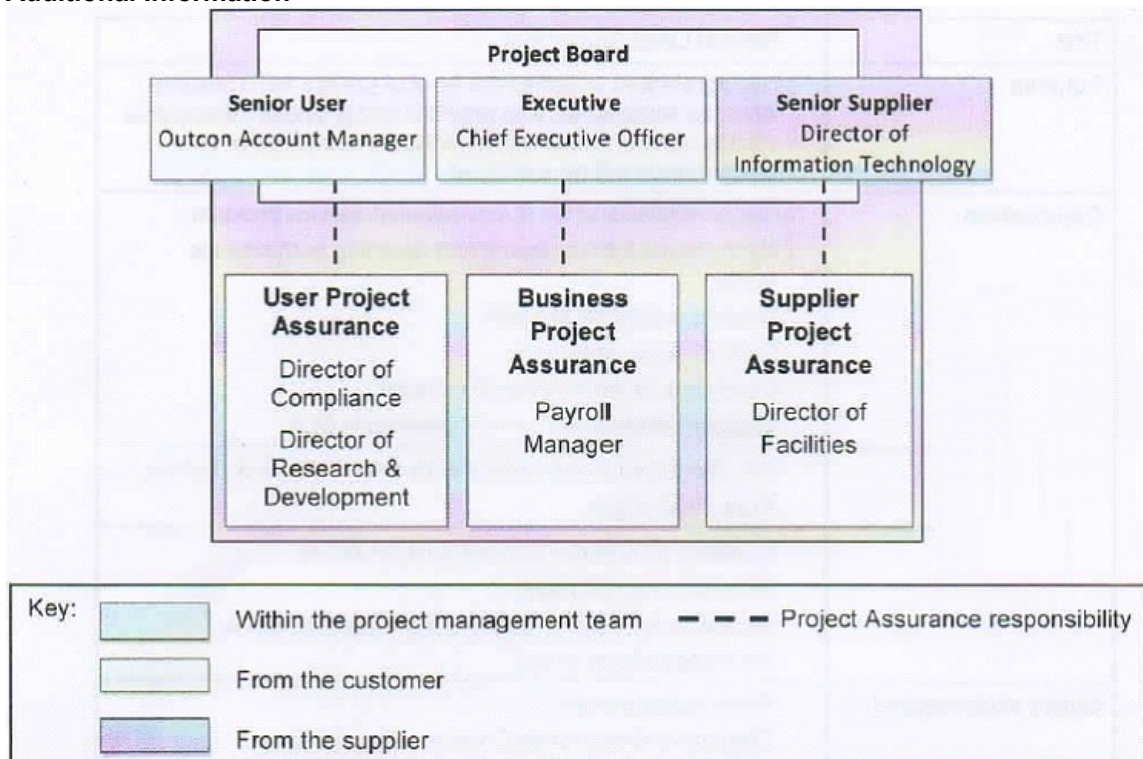

Further information on some resources who could be involved in the project:

Outcome Account Manager: He represents Outcome which is a recruitment agency that provides specialist outsourcing resources. Outcome provided the consultants who carried out the feasibility

[Download Full Version Prince2-Practitioner Exam Dumps\(Updated in Feb/2023\)](#)

study and the same consultants will be providing support and guidance to the Information Technology and Facilities teams during the project.

Director of Finance Division: She was transferred from the Information Technology Division 12 months ago. She is responsible for ensuring a cost-conscious approach is adopted in all operational and project activities across the Ministry of Food Hygiene.

Hardware Manager: Reports to the Director of Information Technology. He provides computer hardware to all business functions but has little awareness of the needs of his colleagues working in software.

Payroll Manager: Reports to the Director of Finance. He is a very experienced and efficient qualified accountant who has much of the responsibility of running the Finance Division on behalf of the Director of Finance. He has been involved in drafting the Ministry's business strategy and assisting in a full business risk assessment. He also drafted the corporate Business Case standards.

Which 2 alternative actions apply to the proposed business assurance for this project?

- A. Remove because he will be impacted by the project and therefore represents a user.
- B. Replace with 'Project Manager' because this is a simple project that does not require additional business assurance.
- C. Add Outcome Consultants' because they carried out the feasibility study.
- D. Add 'Director of Finance Division' because she is responsible for checking that any supplier and contractor payments are authorized.
- E. Retain because he is familiar with the Ministry of Food Hygiene business strategy, the business level risk assessment and the Business Case standards.

Correct Answer: DE

QUESTION 33

Additional Information

Chief Executive Officer (CEO): He started the company 25 years ago and knows his job very well. He injured his leg two years ago which has restricted his visits to the engineering area. As CEO he has an overall perspective of the business strategic requirements and the authority to commit resources as required.

Marketing Director: She has been with the company for three years, following a successful career with a publicity company. She has the ability to represent the needs of the business, particularly as this is a marketing project. She has the authority to commit the annual business marketing budget, from which the project will be funded, as she sees appropriate. She will be responsible for monitoring the expected benefits of the calendar, in particular the improvement of the company's image.

Engineering Manager: He has been responsible for many engineering innovations in the company and is still as keen and energetic as the day he started. Whilst he will not be part of the project team, his staff will feature in the photos for the promotional calendar.

Central Records: This group of five staff looks after all company records and document control. They now maintain all project files.

Bright Lights: This is the local office supplies company. It supplies all the stationery and office equipment needs of the company and will supply the stationery for this project.

Portraits Ltd: This is a professional photographic company with a number of excellent
