

**[Download Full Version Prince2-Practitioner Exam Dumps\(Updated in Feb/2023\)](#)**

(All entries are true statements but may not be shown under the correct heading or in the correct document).

Plan description	1. Stage 3 is the final stage of the project and will deliver the photos, the label design competition entries, the winning label design and the prepared calendar pack.
Plan prerequisites	2. Increase in orders and improved company image. 3. The production cost forecast must be acceptable to the Project Board if the photography and label design competition are to go ahead. 4. The customer list is accurate and complete.
External dependencies	5. A separate project has been reviewing the company's branding. The company logo, required for the label design competition, is being updated. The new company logo is to be supplied by the other project in two weeks time. 6. Customer details will be supplied from the Accounts department and the Marketing department customer databases for the customer list. 7. The label design must contain the new company logo.
Planning assumptions	8. A suitable entry will be received from the label design competition. 9. The photo session schedule created two weeks ago correctly reflects the availability of the engineering staff. 10. Each photo must feature different members of the Engineering team.
Monitoring and control	11. The Project Plan is to be updated with actual throughout the stage. 12. A Highlight Report will be created for the Project Board every two weeks. 13. The Stage Plan will be reviewed at the end of each day, to assess forecast against actual. 14. Product Status Accounts will be produced by Project Support, at the request of the Project Manager, to summarize current and historical data concerning each of the project's products.
Budgets	15. Cost £5k for specialist products 16. Time 4 weeks 17. Risk £0

Using the Project Scenario and the Extract from Stage Plan for stage 3 provided as additional information for this question in the Scenario Booklet, answer the following 5 questions.

The Stage Plan for stage 3 has been produced.

The Engineering Manager insists that there are to be no interruptions to operations whilst photographs are being taken of the engineering staff performing their everyday duties and operating machinery. Two weeks ago the professional photographer produced the photo session schedule based on the operational staff schedule. The operational staff schedule is produced weekly and maintained by the Engineering Manager.

## **[Download Full Version Prince2-Practitioner Exam Dumps\(Updated in Feb/2023\)](#)**

None of the £500 change budget has been used to date and this is available for the stage.

Which 2 statements apply to the External dependencies section?

- A. Delete entry 5 because the new company logo is being delivered by a separate project and will be detailed in the plans for that project.
- B. Move entry 5 to Plan prerequisites because the new company logo will influence the label designs.
- C. Move entry 5 to Plan description because the new company logo will be delivered during stage 3.
- D. Delete entry 6 because the customer details were used in stage 2 to create the customer list.
- E. Delete entry 7 because it should be shown in the Product Description for the label design.

**Correct Answer:** DE

### **QUESTION 84**

Which of the following is not part of the composition of a Plan?

- A. Pre-requisites
- B. Assumptions
- C. Quality responsibilities
- D. Product descriptions

**Correct Answer:** C

### **QUESTION 85**

**HOTSPOT**


#### **Product Summary**

A list of customers will be collated. This will use existing information from the Accounts department about current customers, and existing information from the Marketing department about prospective customers.

Using the tariff of mailing costs available from the Post Office, a production cost forecast will be produced to allow the CEO and the Marketing Director to decide whether to continue with the project. If they decide to continue, they will give the approval to launch the internal label design competition. Competition rules will be required to communicate details of the competition to the staff. The chosen label design will then be selected from the competition entries.

The photos for the calendar must be based on existing photo design ideas available from the Marketing department. The selected photos will be chosen from these. Monthly calendar displays will be created to show the required layout of each page.

**Product Breakdown Structure (contains errors)**

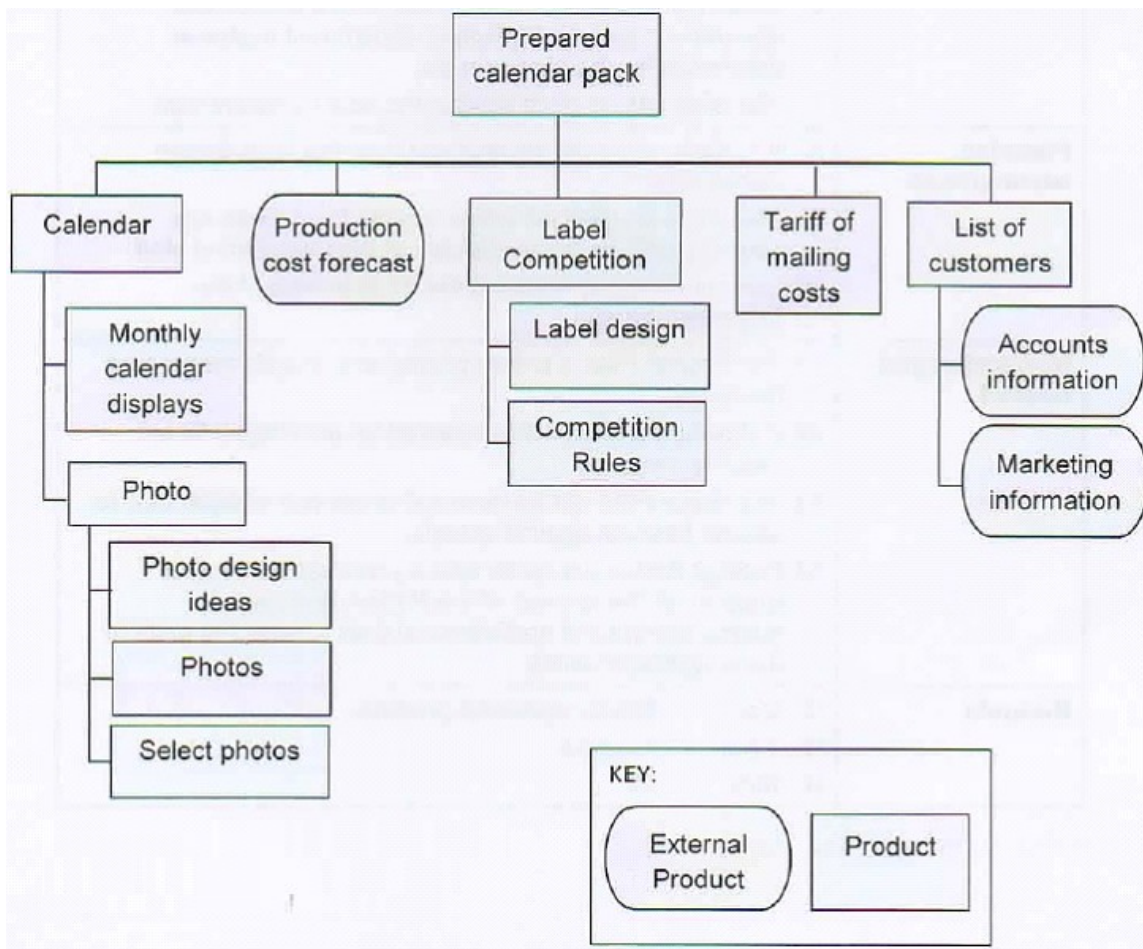

**Extract from Stage Plan for stage 3.**

(All entries are true statements but may not be shown under the correct heading or in the correct document).

[Download Full Version Prince2-Practitioner Exam Dumps\(Updated in Feb/2023\)](#)

Plan description	1. Stage 3 is the final stage of the project and will deliver the photos, the label design competition entries, the winning label design and the prepared calendar pack.
Plan prerequisites	2. Increase in orders and improved company image. 3. The production cost forecast must be acceptable to the Project Board if the photography and label design competition are to go ahead. 4. The customer list is accurate and complete.
External dependencies	5. A separate project has been reviewing the company's branding. The company logo, required for the label design competition, is being updated. The new company logo is to be supplied by the other project in two weeks time. 6. Customer details will be supplied from the Accounts department and the Marketing department customer databases for the customer list. 7. The label design must contain the new company logo.
Planning assumptions	8. A suitable entry will be received from the label design competition. 9. The photo session schedule created two weeks ago correctly reflects the availability of the engineering staff. 10. Each photo must feature different members of the Engineering team.
Monitoring and control	11. The Project Plan is to be updated with actual throughout the stage. 12. A Highlight Report will be created for the Project Board every two weeks. 13. The Stage Plan will be reviewed at the end of each day, to assess forecast against actual. 14. Product Status Accounts will be produced by Project Support, at the request of the Project Manager, to summarize current and historical data concerning each of the project's products.
Budgets	15. Cost £5k for specialist products 16. Time 4 weeks 17. Risk £0

Using the Product Summary and Product Breakdown Structure provided as additional Information for this question In the Scenario Booklet, answer the following question.

Column 1 is a list of some of the entries in the product breakdown structure. Determine whether each entry in Column 1 has been correctly shown in the product breakdown structure. Select from Column 2 the appropriate statement that correctly describes that entry. Each selection from Column 2 can be used once, more than once or not at all.



Column 1	Column 2
Production cost forecast	<div><div></div><div>External product incorrectly shown Internal product incorrectly shown as an external product NOT a product Correctly shown entry</div></div>
Tariff of mailing costs	<div><div></div><div>External product incorrectly shown Internal product incorrectly shown as an external product NOT a product Correctly shown entry</div></div>
Photo design ideas	<div><div></div><div>External product incorrectly shown Internal product incorrectly shown as an external product NOT a product Correctly shown entry</div></div>
Accounts information	<div><div></div><div>External product incorrectly shown Internal product incorrectly shown as an external product NOT a product Correctly shown entry</div></div>
Monthly calendar displays	<div><div></div><div>External product incorrectly shown Internal product incorrectly shown as an external product NOT a product Correctly shown entry</div></div>
Label design	<div><div></div><div>External product incorrectly shown Internal product incorrectly shown as an external product NOT a product Correctly shown entry</div></div>
Select photos	<div><div></div><div>External product incorrectly shown Internal product incorrectly shown as an external product NOT a product Correctly shown entry</div></div>

**Correct Answer:**
